

SmartOrder

Enhancing the Jahez Delivery Application

IS 350 – Project Management | Section 6C2 | Group No. 5

Shahad Fahad Al-Husayni – 445008705

Ghala Saad Al-Mutairi – 445008843

Raneem Aqel Al-Mutairi – 445008776

Lamees Ahmed Al-Faraj – 445009065

Batool Khaled Al-Kan'ani – 445008681



Contents:

01 Introduction

02 Problem Statement

03 Methodology

04 Project Charter

05 Project Requirements

06 Scope Statement

07 WBS & WBS Dictionary

08 RACI Chart

09 Gantt Chart

10 Risk Register

01

Introduction

Introduction

Food delivery apps have become widely used, especially in Saudi Arabia. **Jahez** is one of the most popular platforms, offering a wide variety of restaurants and delivery services.

Affordability

University students need more affordable meal options not supported by current apps

Budget Control

No built-in tools to manage or filter by spending limits

Discovery

No smart suggestions when desired items are unavailable or out-of-budget

Group Orders

Manual coordination of group orders leads to errors and delays

→ *This project proposes SmartOrder — an enhanced version of Jahez with targeted features for modern users.*

02

Problem Statement

Problem Statement

Jahez uses a "one-size-fits-all" model that fails to address the needs of its largest demographic: university students.

No Student Discounts

No verified student discount system — financial accessibility gap for budget-limited students.

No Budget Control

Users cannot set spending limits, leading to poor financial management during ordering.

Poor Search Discovery

When an item is unavailable, the system fails to suggest intelligent alternatives.

Group Order Friction

Manual group order coordination causes errors, delays, and no integrated bill splitting.



SmartOrder bridges these gaps — transforming a generic delivery tool into a personalized, cost-effective, and socially integrated platform.

03


Methodology

INCREMENTAL MODEL



Methodology — Incremental Software Development Model

The project adopts the Incremental Software Development Model — each increment adds new functionality.

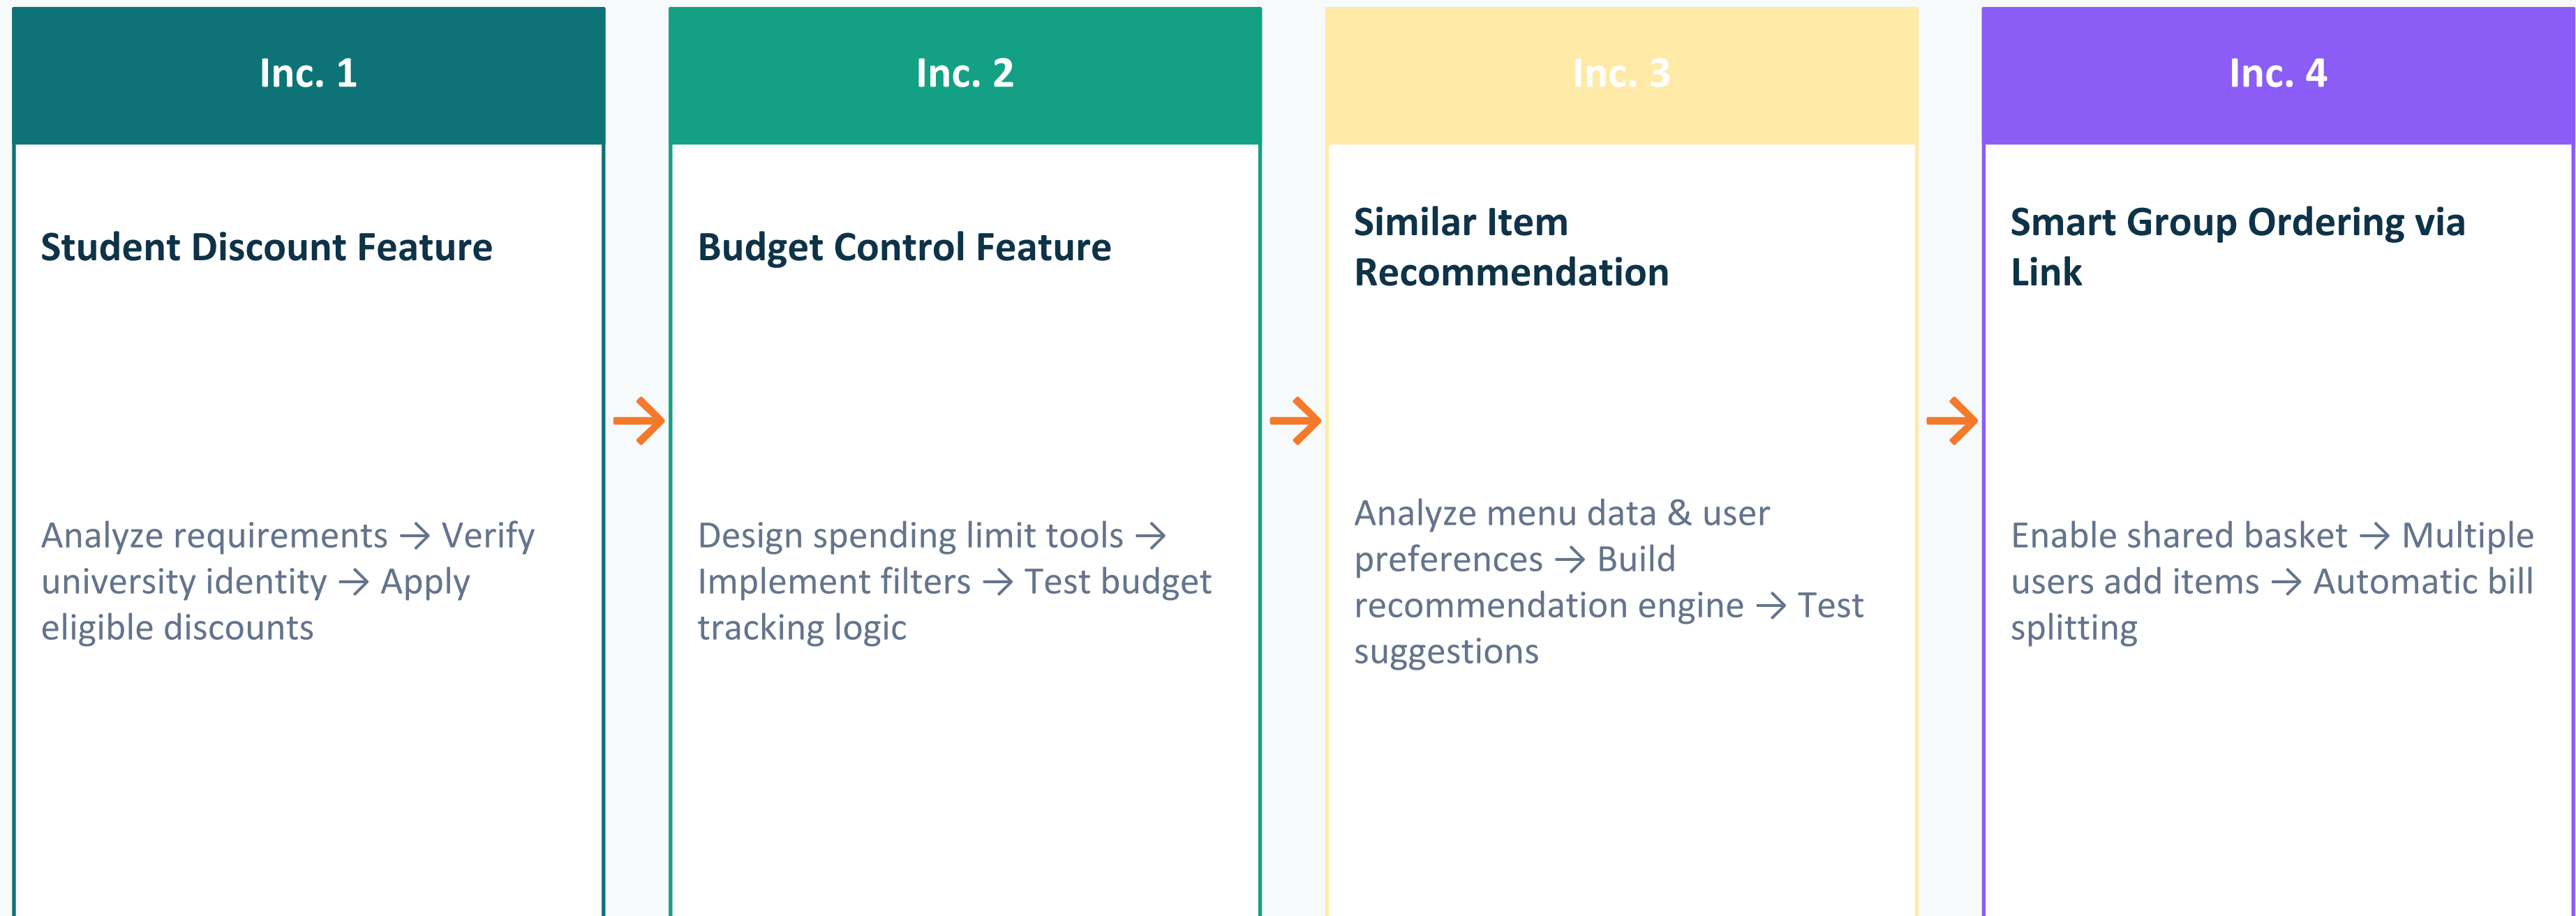

Why incremental? — Each feature is developed, tested, and evaluated independently before adding the next, ensuring better project management and continuous improvement.

04

Project Charter

Project Charter — Overview

Field	Details
Project Title	SmartOrder: Enhancing the Jahez Delivery Application
Authorization Date	March 1, 2026
Start Date	March 1, 2026
Projected Finish	December 1, 2026
Budget	1,000,000 SAR (additional funds may be approved if needed)
Project Manager	Lamees Al-Faraj — Imees.alfaraj@smartorder.com — 0506557897
Project Sponsor	CEO of Jahez International Company

Project Charter — Objectives & Milestones

Project Objectives

- Improve UI/UX and order processing speed
- Rebrand the app from Jahez to SmartOrder
- Add student discounts for university students
- Add budget tracking — set and monitor spending
- Add similar item suggestions across restaurants
- Add group ordering via a shareable link
- Support Arabic and English languages

Key Milestones

Sep 1, 2026

Student Discount Feature

Sep 15, 2026

Budget Tracking Feature

Oct 11, 2026

Similar Items Suggestion

Oct 20, 2026

Group Orders via Link

Nov 17, 2026

Final Testing & Bug Fixing

Dec 1, 2026

App Launch

Project Charter

Budget Information:	The firm has allocated 1 million SAR for this project. Additional funds may be available if needed. The project will rely on internal labor for software development, and third-party services will be outsourced for specific features such as payment integration or advanced AI functionalities.
Project Manager:	Lmees Al-Faraj, 0506557897, lmees.alfaraj@smartorder.com
Project Objectives:	The goal of this project is to improve the Jahez app by making the interface and user experience better. We also plan to add some new features to make the app more useful for users. These features include student discounts to give university students special offers, a budget tracking feature so users can set and monitor their spending, suggestions for similar items based on what the user is ordering, and a group order feature where users can share a link so others can join the same order. In addition, the app will have a new name. The name will change from “Jahez” to “SmartOrder.” We will also focus on making the UI/UX easier to use and improving the speed of order processing so users can have a smoother and faster experience when using the app.

Main Project Success Criteria:	• The app must meet all functional and non-functional specifications. • All features must be tested, and the app must function smoothly with no critical bugs. • The app must be launched on schedule and meet customer expectations regarding usability and performance. • The CEO will formally approve the app’s launch with feedback from key stakeholders.
Approach :	
The project team was organized by assigning a specific role to each member. This helped divide the tasks effectively and made the project easier to manage. After that, we reviewed the current Jahez application to understand how it works and to identify areas that could be improved. After that, we suggested several features that could help students when using the app. These include student discounts, a budget filter that allows users to find meals within their budget, suggestions for similar items, and a group order feature where one person can send a link so others can add their orders and pay individually. Then we will prepare a simple project plan. This will include the Work Breakdown Structure (WBS), the scope statement, and a timeline so we know what tasks need to be done and when. During the project, we will meet to discuss our progress and make sure everything is going well. We will also keep notes about the work we do and the ideas or solutions we come up with, and all of that will be included in the final report.	

Project Charter

ROLES AND RESPONSIBILITIES

Name	Role	Position	Contact Information
Jahez	Project Sponsor	CEO	support@jahez.net
Lmees Al-Faraj	Project Manager	Manager	lmees.al-faraj@smartorder.com
Patol Al-Kanani	Team Member	App Developer	patol.alkanani@smartorder.com
Ghala Al-Mutairi	Team Member	UI/UX Designer	ghala.almutairi@smartorder.com
Shahad Al-Husayni	Team Member	Backend Developer	shahad.alhusayni@smartorder.com
Raneem Al-Mutairi	Team Member	Programmer	raneem.almutairi@smartorder.com

Sign-off: (Signatures of all the above stakeholders)

Lmees AlFaraj

Patol Al-Kanani

Ghala Al-Mutairi

Shahad Al-Husayni

Raneem Al-Mutairi

Comments:

- Lmees Al-faraj, Project Manager:

“This project is a critical milestone for SmartOrder. Collaboration and timely delivery are key to its success.”

- Patol Al-kanani, App Developer:

“The new features like student discounts and group orders will significantly improve user engagement and satisfaction.”

- Ghala Al-Mutairi, UI/UX Designer:

“Focus will be on making the app intuitive and user-friendly, ensuring all new features are seamless.”

- Shahad Al-Husayni, Backend Developer:

“I will ensure the backend supports the app’s new features while maintaining speed and reliability.”

- Raneem Al-Mutairi, Programmer:

“I will work on making the code efficient and ensure compatibility with the app’s updated features.”

Project Charter — Team Roles & Responsibilities

Role	Name	Responsibilities
Project Sponsor (CEO)	Jahez International	Strategic guidance, final approval authority
Project Manager	Lamees Al-Faraj	Timeline management, coordination, deliverables
App Developer	Batool Al-Kan'ani	Core feature programming & integration, app store submission
UI/UX Designer	Ghala Al-Mutairi	Visual layout, UAT, post-launch review
Backend Developer	Shahad Al-Husayni	Server-side infrastructure, DB & cloud design, monitoring
Programmer	Raneem Al-Mutairi	Efficient code, AI engine lead, integration testing

05

Project Requirements

Project Requirements — Stakeholder Elicitation Techniques

Interviews

Stakeholders: CEO & Regulatory Authorities

Strategic insights, compliance requirements, alignment with business goals & data privacy.

Observation

Stakeholders: University Students

Reveals real social coordination challenges in budget management & group ordering.

Questionnaires

Stakeholders: End-Users & Marketing Team

Validate demand for Similar Item Recommendations and Student Discount incentives.

Focus Groups

Stakeholders: Dev Team (UI/UX) & QA Team

Resolve integration challenges between backend (budget tracking) and UI (group ordering).


System & Hardware Requirements

System Requirements

- Mobile app — Android & iOS compatible
- Secure RESTful API integration with Jahez backend
- University email verification module
- AI-based recommendation engine
- Shared basket service via shareable link
- Third-party payment gateway with bill splitting
- Arabic & English language support

Hardware Requirements

- Smartphones: min. 2 GB RAM & 100 MB storage
- Cloud-hosted backend with auto-scaling
- Active internet connection required
- Database server for client data & case information

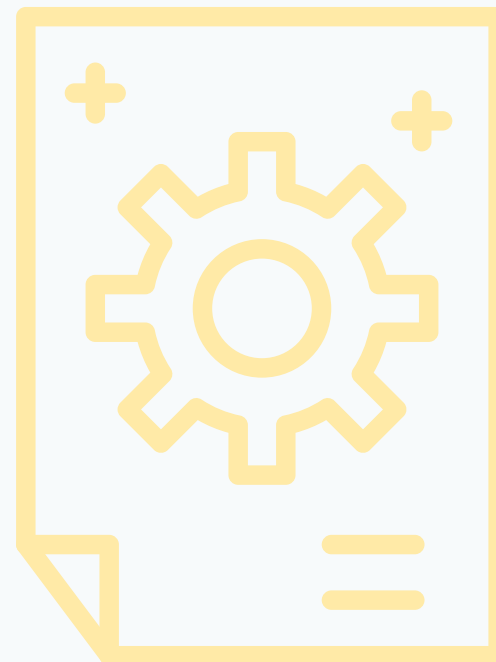

Functional Requirements

FR1

Student Discount

Students verify university affiliation → eligible discounts applied automatically at checkout.

FR4

Group Ordering via Link

User creates a group session & shares a link → others join, add items, and pay their individual share.

FR2

Budget Selection

Users set a spending limit → system filters and displays only meals within that budget.

FR5

User Authentication

Users register, log in, and manage profiles securely.

FR3

Similar Item Suggestions

When an item is unavailable or out of budget → system displays similar items sorted by relevance & price.

FR6

Order Tracking

Users track real-time order status from placement to delivery.

Non-Functional Requirements

NFR1 — Performance

App loads and responds within 2 seconds under normal network conditions.

NFR2 — Scalability

Backend supports up to 10,000 concurrent users without performance degradation.

NFR3 — Security

Strong security protocols to protect user data and ensure compliance with relevant laws.

NFR4 — Usability

Interface achieves a System Usability Scale (SUS) score of 80 or above in user testing.

NFR5 — Availability

System maintains 99.5% uptime, with planned maintenance not exceeding 2 hours/month.

NFR6 — Maintainability

Modular codebase design allows easy updates without system downtime.

NFR7 — Compliance

Complies with Saudi data protection regulations and Google Play & Apple App Store policies.

06

Scope Statement

Scope Statement — Description & Deliverables

Project :

SmartOrder: Enhancing the Jahez Delivery Application **Date Prepared** : March 1,2026

Project Scope Description

Enhance the current Jahez delivery application by improving UI/UX and order processing speed.

Rebrand from Jahez to SmartOrder. Main features: student discounts, budget tracking, similar item suggestions, group ordering via shared link.

Project Deliverables

- Updated app name and improved UI/UX design
- Student discount feature — due Sep 1, 2026
- Budget tracking feature — due Sep 15, 2026
- Similar items suggestion feature — due Oct 11, 2026
- Group order feature via shared link — due Oct 20, 2026
- Final testing, bug fixing & launch approval package — due Dec 1, 2026

Product Acceptance Criteria

All functional & non-functional requirements complete with no critical bugs • Usability & performance meet customer expectations • CEO & key stakeholders formally approve the launch

Scope Statement — Exclusions, Constraints & Assumptions

Project Exclusions

- Redesigning all Jahez business operations outside the mobile application
- Restaurant-side inventory, pricing, or menu management systems
- Delivery driver logistics, fleet management, or hardware changes
- Long-term post-launch maintenance beyond final testing and bug fixing

Project Constraints

- Budget limited to 1 million SAR
- Timeline: March 1 – December 1, 2026
- Each major feature must meet its milestone date
- Primarily internal labor for software development
- Third-party services for payment/AI may be needed

Project Assumptions

- Team members available to complete assigned roles
- Stakeholders provide timely feedback and approvals
- Jahez backend can support planned enhancements
- Third-party payment/AI services are compatible
- Student eligibility can be verified for discounts
- Users have compatible devices & internet access

07

WBS & WBS Dictionary

Work Breakdown Structure (WBS)

WBS Structure — 7 Main Phases

1 1 Project Initiation	1 2 Gathering Requirements	1 3 System Design	1 4 System Development	1 5 System Testing	1 6 System Deployment	1 7 Documentation & Closure
Charter Dev.	Elicitation	UI/UX Design	Student Discount	Integration	App Store Sub.	Handover
Stakeholder ID	Functional Req.	Tech Architecture	Budget Control	UAT	Launch Approval	Post-Launch Rev.
Strategic Align.	Non-Functional	DB & Cloud	AI Recommend.	Bug Fixing	Production Mon.	Admin Closure
			Group Ordering			

WBS Dictionary (Phase 1.1 – 1.3)

WBS	Work	Activities	Resources	Cost	Criteria	Manager
1.1.1	Project Charter Development	Create formal document authorizing project, defining 1M SAR budget, goals & stakeholders	MS Word, Meeting Room	20,000 SAR	Document signed by the CEO	Project Manager
1.1.2	Stakeholder Identification	Identify all team members and assign roles (PM, Developers, Designers)	MS Excel, Stakeholder Register	10,000 SAR	All key roles clearly assigned	Project Manager
1.1.3	Strategic Alignment	Ensure Jahez → SmartOrder rebranding aligns with business objectives	Meeting tools, Corporate data	20,000 SAR	Formal approval of transition strategy	Project Manager
1.2.1	Stakeholder Elicitation	Interviews with CEO + surveys/observations with university students	Survey tools, Target Audience	40,000 SAR	500+ valid survey responses	Project Manager
1.2.2	Functional Requirements	Define & document system behaviors (discounts, budget filters, etc.)	Requirements template	30,000 SAR	FR document reviewed & approved	Project Manager
1.2.3	Non-Functional Requirements	Establish quality standards: 2-sec response time, security protocols	Technical documentation	30,000 SAR	NFR doc signed by technical team	Backend Dev & Programmer
1.3.1	UI/UX Design	Design application interface & visual assets for rebranded experience	Figma, UI/UX tools	60,000 SAR	Final mockups approved by PM	UI/UX Designer
1.3.2	Technical Architecture	Plan backend structure including RESTful APIs & email verification	System design tools	50,000 SAR	Architecture diagram reviewed & approved	Backend Developer

WBS Dictionary (Phase 1.4 – 1.5)

WBS	Work	Activities	Resources	Cost	Criteria	Manager
1.3.3	Database & Cloud Design	Design DB schema & cloud infrastructure for 10,000 concurrent users	Cloud hosting platform	40,000 SAR	Database schema successfully deployed	Backend Developer
1.4.1	Student Discount Feature	Develop university identity verification & discount application logic	IDEs, Dev frameworks	100,000 SAR	Feature passes initial unit testing	App Dev, Backend Dev, Programmer
1.4.2	Budget Control Feature	Implement spending limit tools and filters for ordering	IDEs, Dev frameworks	100,000 SAR	Budget filter operates without logic errors	App Dev, Backend Dev, Programmer
1.4.3	AI Recommendation Engine	Build system to suggest alternative items by price/preferences	AI/ML datasets, Menu data	100,000 SAR	Engine correctly outputs relevant alternatives	App Developer, Programmer
1.4.4	Group Ordering Module	Develop shareable link functionality for collaborative ordering with bill splitting	IDEs, Dev frameworks	100,000 SAR	Multiple users can successfully split a single bill	App Dev, Backend Dev, Programmer
1.5.1	Integration Testing	Verify all features interact correctly with backend & existing systems	Testing env., QA tools	60,000 SAR	Zero critical defects in integration tests	App Dev, Backend Dev, Programmer
1.5.2	User Acceptance Testing (UAT)	Testing sessions with university students to validate satisfaction	Beta app, Student testers	50,000 SAR	User satisfaction score $\geq$ 80	UI/UX Designer

WBS Dictionary (Phase 1.6 – 1.7)

WBS	Work	Activities	Resources	Cost	Criteria	Manager
1.5.3	Final Bug Fixing	Identify and resolve critical bugs before official launch	Bug tracking (Jira)	40,000 SAR	All critical & major bugs resolved	App Dev, Backend Dev, Programmer
1.6.1	App Store Submission	Prepare & submit app to Google Play & Apple App Store	Developer Accounts	30,000 SAR	App approved by both stores	App Developer
1.6.2	Launch Approval	Obtain formal sign-off from CEO & key stakeholders	Presentation tools	20,000 SAR	Formal sign-off to go live	Project Manager
1.6.3	Production Monitoring	Monitor system performance post-launch for 99.5% uptime	Server monitoring tools	50,000 SAR	System maintains 99.5% uptime	Backend Dev & Programmer
1.7.1	Project Handover	Finalize project report & technical docs for department handover	MS Word, Project Docs	20,000 SAR	Final report accepted by instructor	Project Manager
1.7.2	Post-Launch Review	Collect & analyze initial user feedback for future updates	Analytics software, App reviews	15,000 SAR	Feedback report generated	UI/UX Designer
1.7.3	Administrative Closure	Formally close project, release team resources, archive all files	Archiving tools	15,000 SAR	Project formally closed & resources freed	Project Manager

08

RACI Chart

RACI Chart

R = Responsible • A = Accountable • C = Consulted • I = Informed

Task / Activity	CEO	PM	App Dev	UI/UX	Backend	Prog.
Project Charter Dev.	A	R	I	I	I	I
Stakeholder Identification	I	A,R				
Strategic Alignment	A	R				
Stakeholder Elicitation		A,R		C		C
Functional Requirements		A,R	C	C	C	C
Non-Functional Req.		A	C		R	R
UI/UX Design		A	C	R		
Technical Architecture	I	A	C		R	C
Database & Cloud Design	I	A			R	C
Student Discount Feature		A	R	C	R	R
Budget Control Feature		A	R	C	R	R
AI Recommendation Engine		A	R	C	C	R
Group Ordering Module		A	R	C	R	R
Integration Testing		A	R		R	R

RACI Chart

R = Responsible • A = Accountable • C = Consulted • I = Informed

User Acceptance Testing	I	A	I	R		
Final Bug Fixing		A	R	C	R	R
App Store Submission	I	A	R			
Launch Approval	A	R				
Production Monitoring		A	C		R	R
Project Handover	I	A,R	I	I	I	I
Post-Launch Review	I	A	C	R	C	C
Administrative Closure	A	R				

RACI — Role Assumptions

CEO (Sponsor)

Provides strategic guidance & holds final approval authority. Informed on technical tasks (Architecture, DB, UAT, App Store Submission) which fall outside sponsor scope.

Project Manager

Manages timeline, coordinates deliverables. Accountable on tech tasks (dev, testing, bug fixing) without executing. Leads handover & oversees post-launch review.

App Developer

Programs & integrates all 4 core features, conducts integration testing, fixes bugs, submits app. Consulted on UI/UX, Architecture, post-launch review.

UI/UX Designer

Develops visual layout, conducts UAT & post-launch review. Consulted on all 4 features and bug fixing to maintain UI consistency.

Backend Developer

Builds server-side infrastructure, manages DB & cloud, supports all features. Responsible for integration testing, bug fixing & production monitoring.


Programmer

Writes efficient code, leads AI engine development, handles integration testing, bug fixing & production monitoring. Consulted on Architecture & Functional Requirements.

09

Gantt Chart

Gantt Chart — SmartOrder Project Timeline

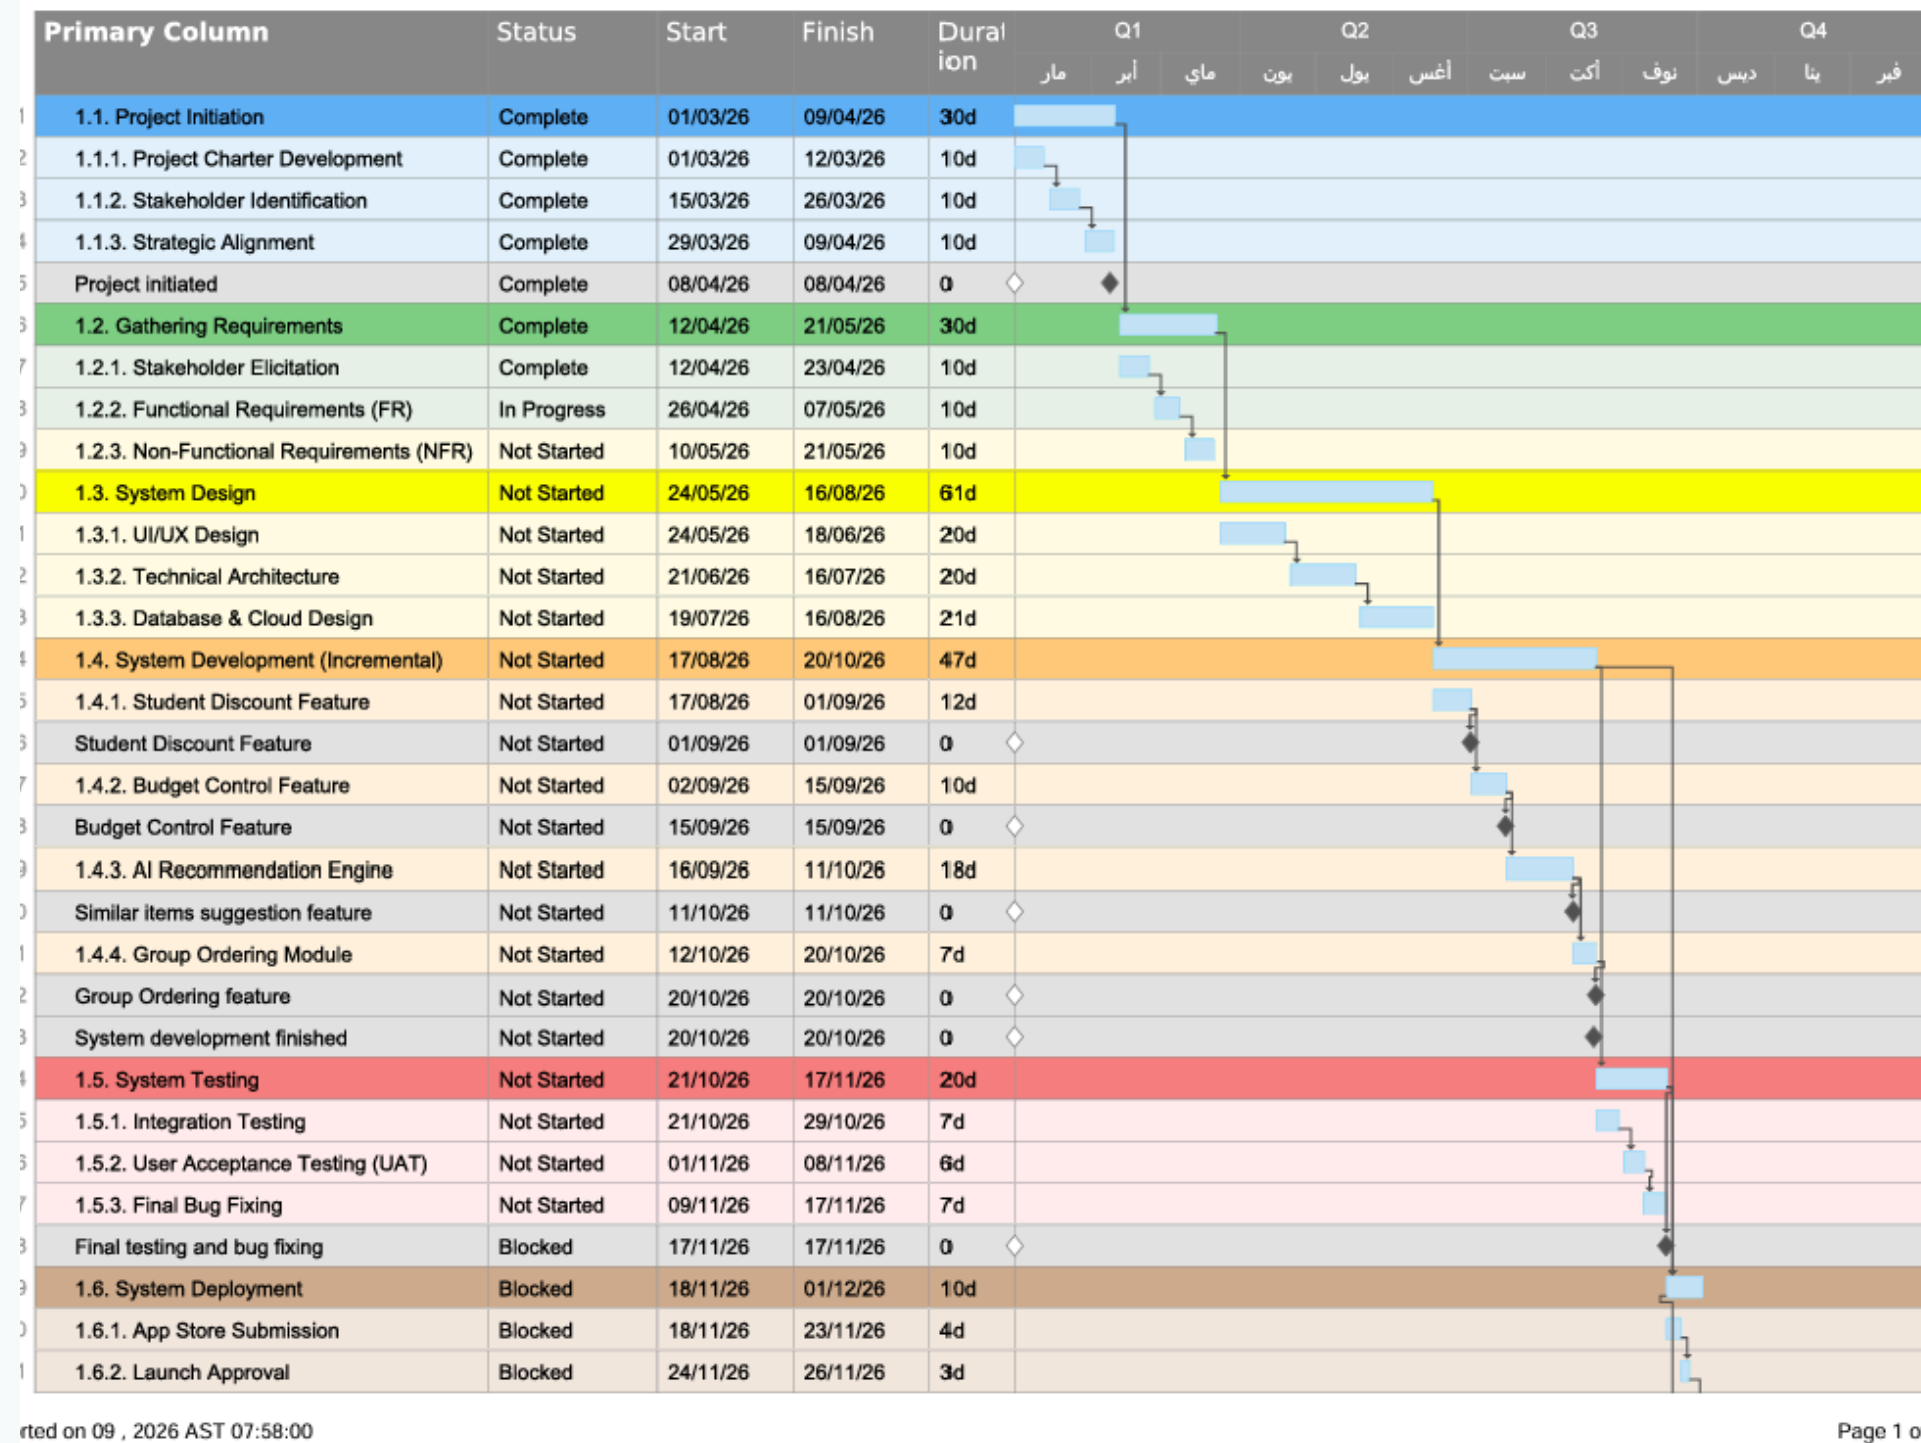

	Primary Column	Status	Start	Finish	Duration	Q1		Q2		Q3		Q4			
						مار	أبر	ماي	يون	يول	أغس	سبتمبر	أكتوبر	نوفمبر	ديسمبر
2	1.6.3. Production Monitoring	Blocked	29/11/26	01/12/26	3d										
3	1.7. Documentation and Closure	Blocked	18/11/26	01/12/26	10d										
4	1.7.1. Project Handover	Blocked	18/11/26	22/11/26	3d										
5	1.7.2. Post-Launch Review	Blocked	23/11/26	26/11/26	4d										
6	1.7.3. Administrative Closure	Blocked	29/11/26	01/12/26	3d										

10

Risk Register

Risk Register — Overview

Rank	ID	Risk Name	Type	Category	Prob.	Impact	Owner	Status
1	R1	API Delay	Negative	Technical	Medium	High	Backend Dev	Open
2	R2	Schedule Slip	Negative	Schedule	Medium	High	Project Manager	Open
3	R5	Feature Success	Positive	Business	Medium	High	Project Manager	Open
4	R4	Sync Fail	Negative	Technical	Low	High	Programmer	Open
5	R7	Budget Logic Error	Negative	Technical	Low	High	Programmer	Open
6	R6	AI Inaccuracy	Negative	Technical	Medium	Medium	App Developer	Open
7	R3	Fast Design	Positive	Schedule	Medium	Medium	UI/UX Designer	Open



Risk Register — Risk Response Details

R1

API Delay

Mitigation: Start backend analysis & setup early → allocate extra time for troubleshooting.

R2

Schedule Slip

Mitigation: Reallocate team effort to critical tasks → hold frequent progress meetings.

R3

Fast Design (+)

Exploitation: Use advanced prototyping templates & UI kits to accelerate design process.

R4

Sync Fail

Mitigation: Conduct rigorous testing & code reviews specifically for group order increment.

R5

Feature Success (+)

Enhancement: Add more resources to expand discount partnerships; ensure seamless performance.

R6

AI Inaccuracy

Mitigation: Train AI model on available data; fallback to top-rated items when confidence is low.

R7

Budget Logic Error

Mitigation: Conduct rigorous unit testing specifically on calculation logic.

Thank You

SmartOrder — Enhancing Jahez for a Smarter Experience

